




Army Test and Evaluation Command

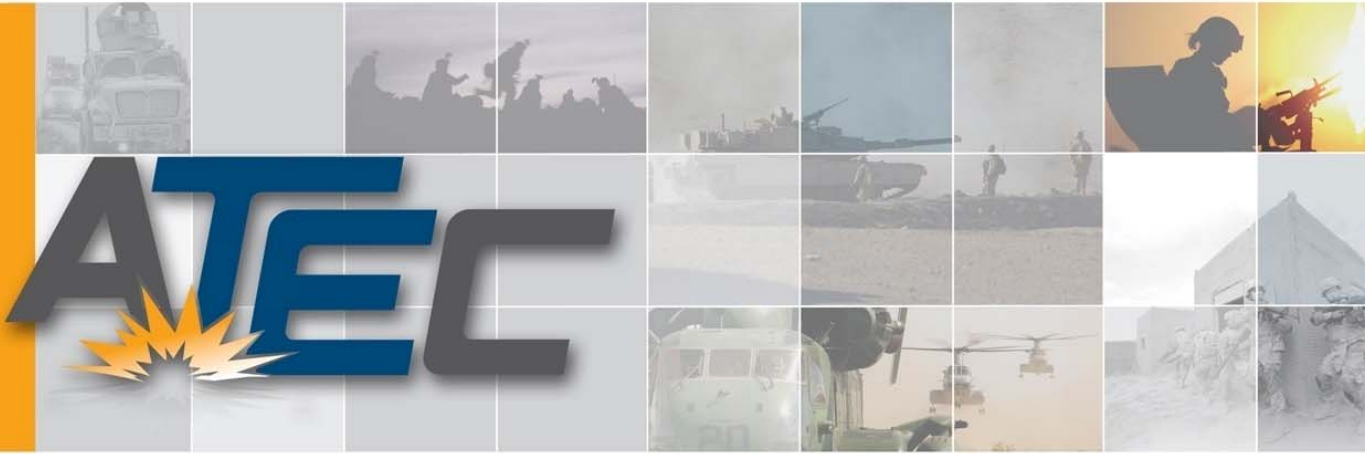

**335** Days to BRAC  
E-Date 15 Sep 2011

# CSSC Update

**ATEC BRAC**  
**14 October 2010**

To keep CSSC informed of  
BRAC actions

# Up Front

- *Conditions are set on APG:*
  - Building on track
  - Preponderance of workforce at APG
  - C2 established at APG
  - Plenty of seats available
  - All New-Hires to APG
- But-- now we have mission concerns-
  - Larger Army has asked us to look at acceleration
    - Resource competition in/around the NCR (strain on personnel, transportation systems)
  - We intend to “do our part”- “although a small part we are still a part”

# Construction



- BoD = 24 Jun 11
- ATEC Ready = 1 Aug 11


- ~ 50% Complete
- Steel Structure is Complete
- Pre-cast Panels are Going Up
- Weather Tight Nov 10



# ToF Status

ATEC		
<b>ATEC</b>	<b>115</b>	<b>ToF's Issued</b>
	<b>101</b>	<b>Accepted</b>
	<b>14</b>	<b>Declined</b>
	<b>9</b>	<b>Departed</b>
	<b>2</b>	<b>Early Moves</b>
AEC		
<b>AEC</b>	<b>94</b>	<b>ToF's Issued</b>
	<b>66</b>	<b>Accepted</b>
	<b>27</b>	<b>Declined</b>
	<b>8</b>	<b>Departed</b>
	<b>9</b>	<b>Early Moves</b>
TOTAL		
<b>TOTAL</b>	<b>209</b>	<b>ToF's Issued</b>
	<b>167</b>	<b>Accepted</b>
	<b>41</b>	<b>Declined</b>
	<b>17</b>	<b>Departed</b>
	<b>11</b>	<b>Early Moves</b>

Priority Placement Program	
Currently Registered	5
Pending Registration	10
Placed	2
Declined Offer	1
Ineligible	2
Retirement	
Plan to Retire	5
Pending Employee Decision	5

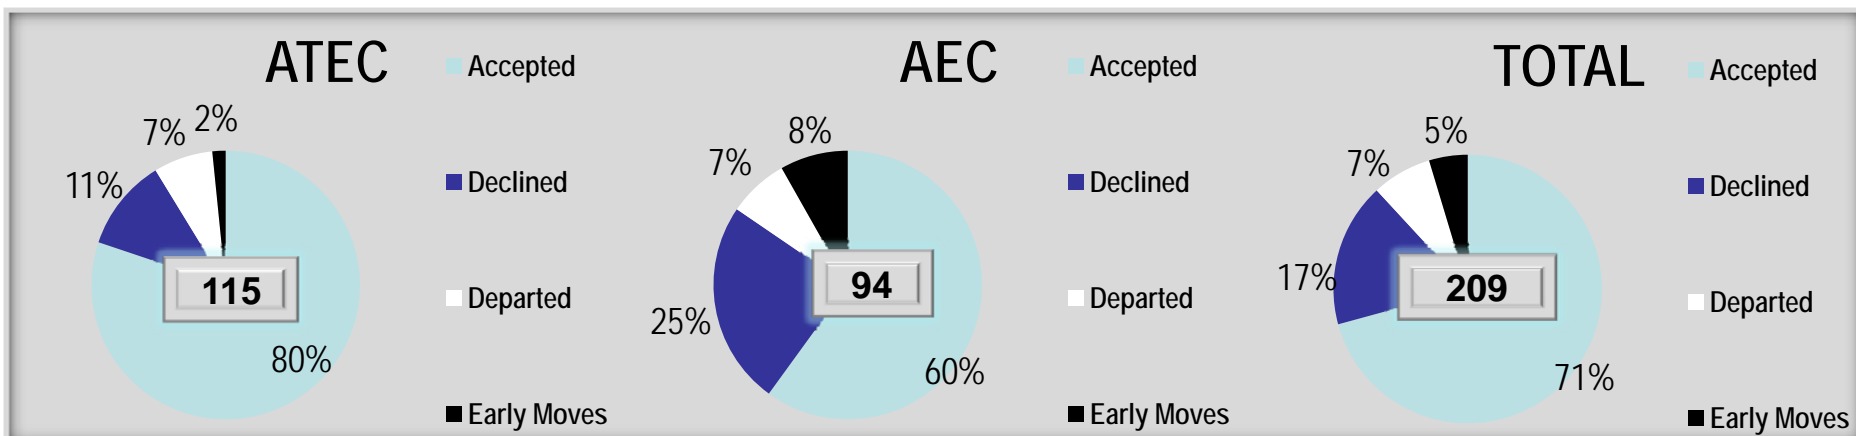

# Current Situation

➤ As Briefed to HQDA 7 Oct

**AMERICA'S ARMY:** UNCLASS/FOUO  
**THE STRENGTH OF THE NATION**

## ATEC Status

---

### VCSABRAC SUMMIT VII

#### Shift Moves Left Status

Quarter	Original Plan (Civilian)	Original Plan (Military)	Moved Left Plan (Civilian)	Moved Left Plan (Military)
1st QTR	~10	~10	~40	~20
2nd QTR	~15	~15	~85	~25
3rd QTR	~20	~20	~70	~25
4th QTR	~100	~40	~30	~10

#### Critical Facilities Status

- On DA Watch List (Tight Timeline):
  - BoD 24 Jun 11
  - SRD 1 Aug 11
- Joint Occupancy Mitigation Strategy (Internal CCIR)
- Temp. Admin Space Adequate

---

#### BRAC Actions Status

Location	Count	Percentage
Alexandria	327	53%
APG	283	47%

- Incoming Cdr to APG (C2 Fwd, 28 Oct 10)
- Preponderance of Workforce at APG
- Initiate Hiring Actions for 40+ Declinations
- Use Open Continuous Announcements to offset reality of interim ToF acceptances
- Accelerating PCS Order Process

*Timely CCIR Reporting*

#### 3rd / 4th Quarter FY11 Movement Timeline



# BRAC Info Sessions

<b>Projected Dates</b> Dependent on Proponent Availability	<b>Proponent</b>	<b>Topic</b>
13 October 2010 Joint w/JPEO-CBD	Harford Community College (HCC)	Home Buying Basics Seminar
26 October 2010	Ft. Belvoir Transportation & HCC	BRAC Transportation and Stress Management Brief
November 2010, April 2011	Corps of Engineers	DNRP/HAP
November 2010, March 2011, May 2011,	DFAS, ATEC/AEC Personnel, RM, Legal; ATEC Personnel Early Moves	PCS & Tax Implications, ATEC/AEC Internal PCS Processes and Requirements; PCS Rules of Engagement; Lessons Learned
December 2010, March 2011	CARE Office	General Priority Placement Program (PPP)
January 2011, April 2011	CPAC	Severance Pay & other placement options; Restored Leave
Will review the ABC VTC conference schedule and provide to the workforce	ABC	Retirement
